

2025 State Water Project Construction Project Updates



November 19, 2025

Dale Brown, P.E., Division Manager

Construction Contracts

Documentation prepared in 2025 (Jan 1 through October 31)

Construction Contracts = 45

Daily Inspection Reports = 7,764

Serial Letters = 579

Contractor Letters = 411

Contractor Payments = 193


RFIs = 1,356

Contractor Payments = 193

Submittals = 3,120



CALIFORNIA DEPARTMENT OF
WATER RESOURCES

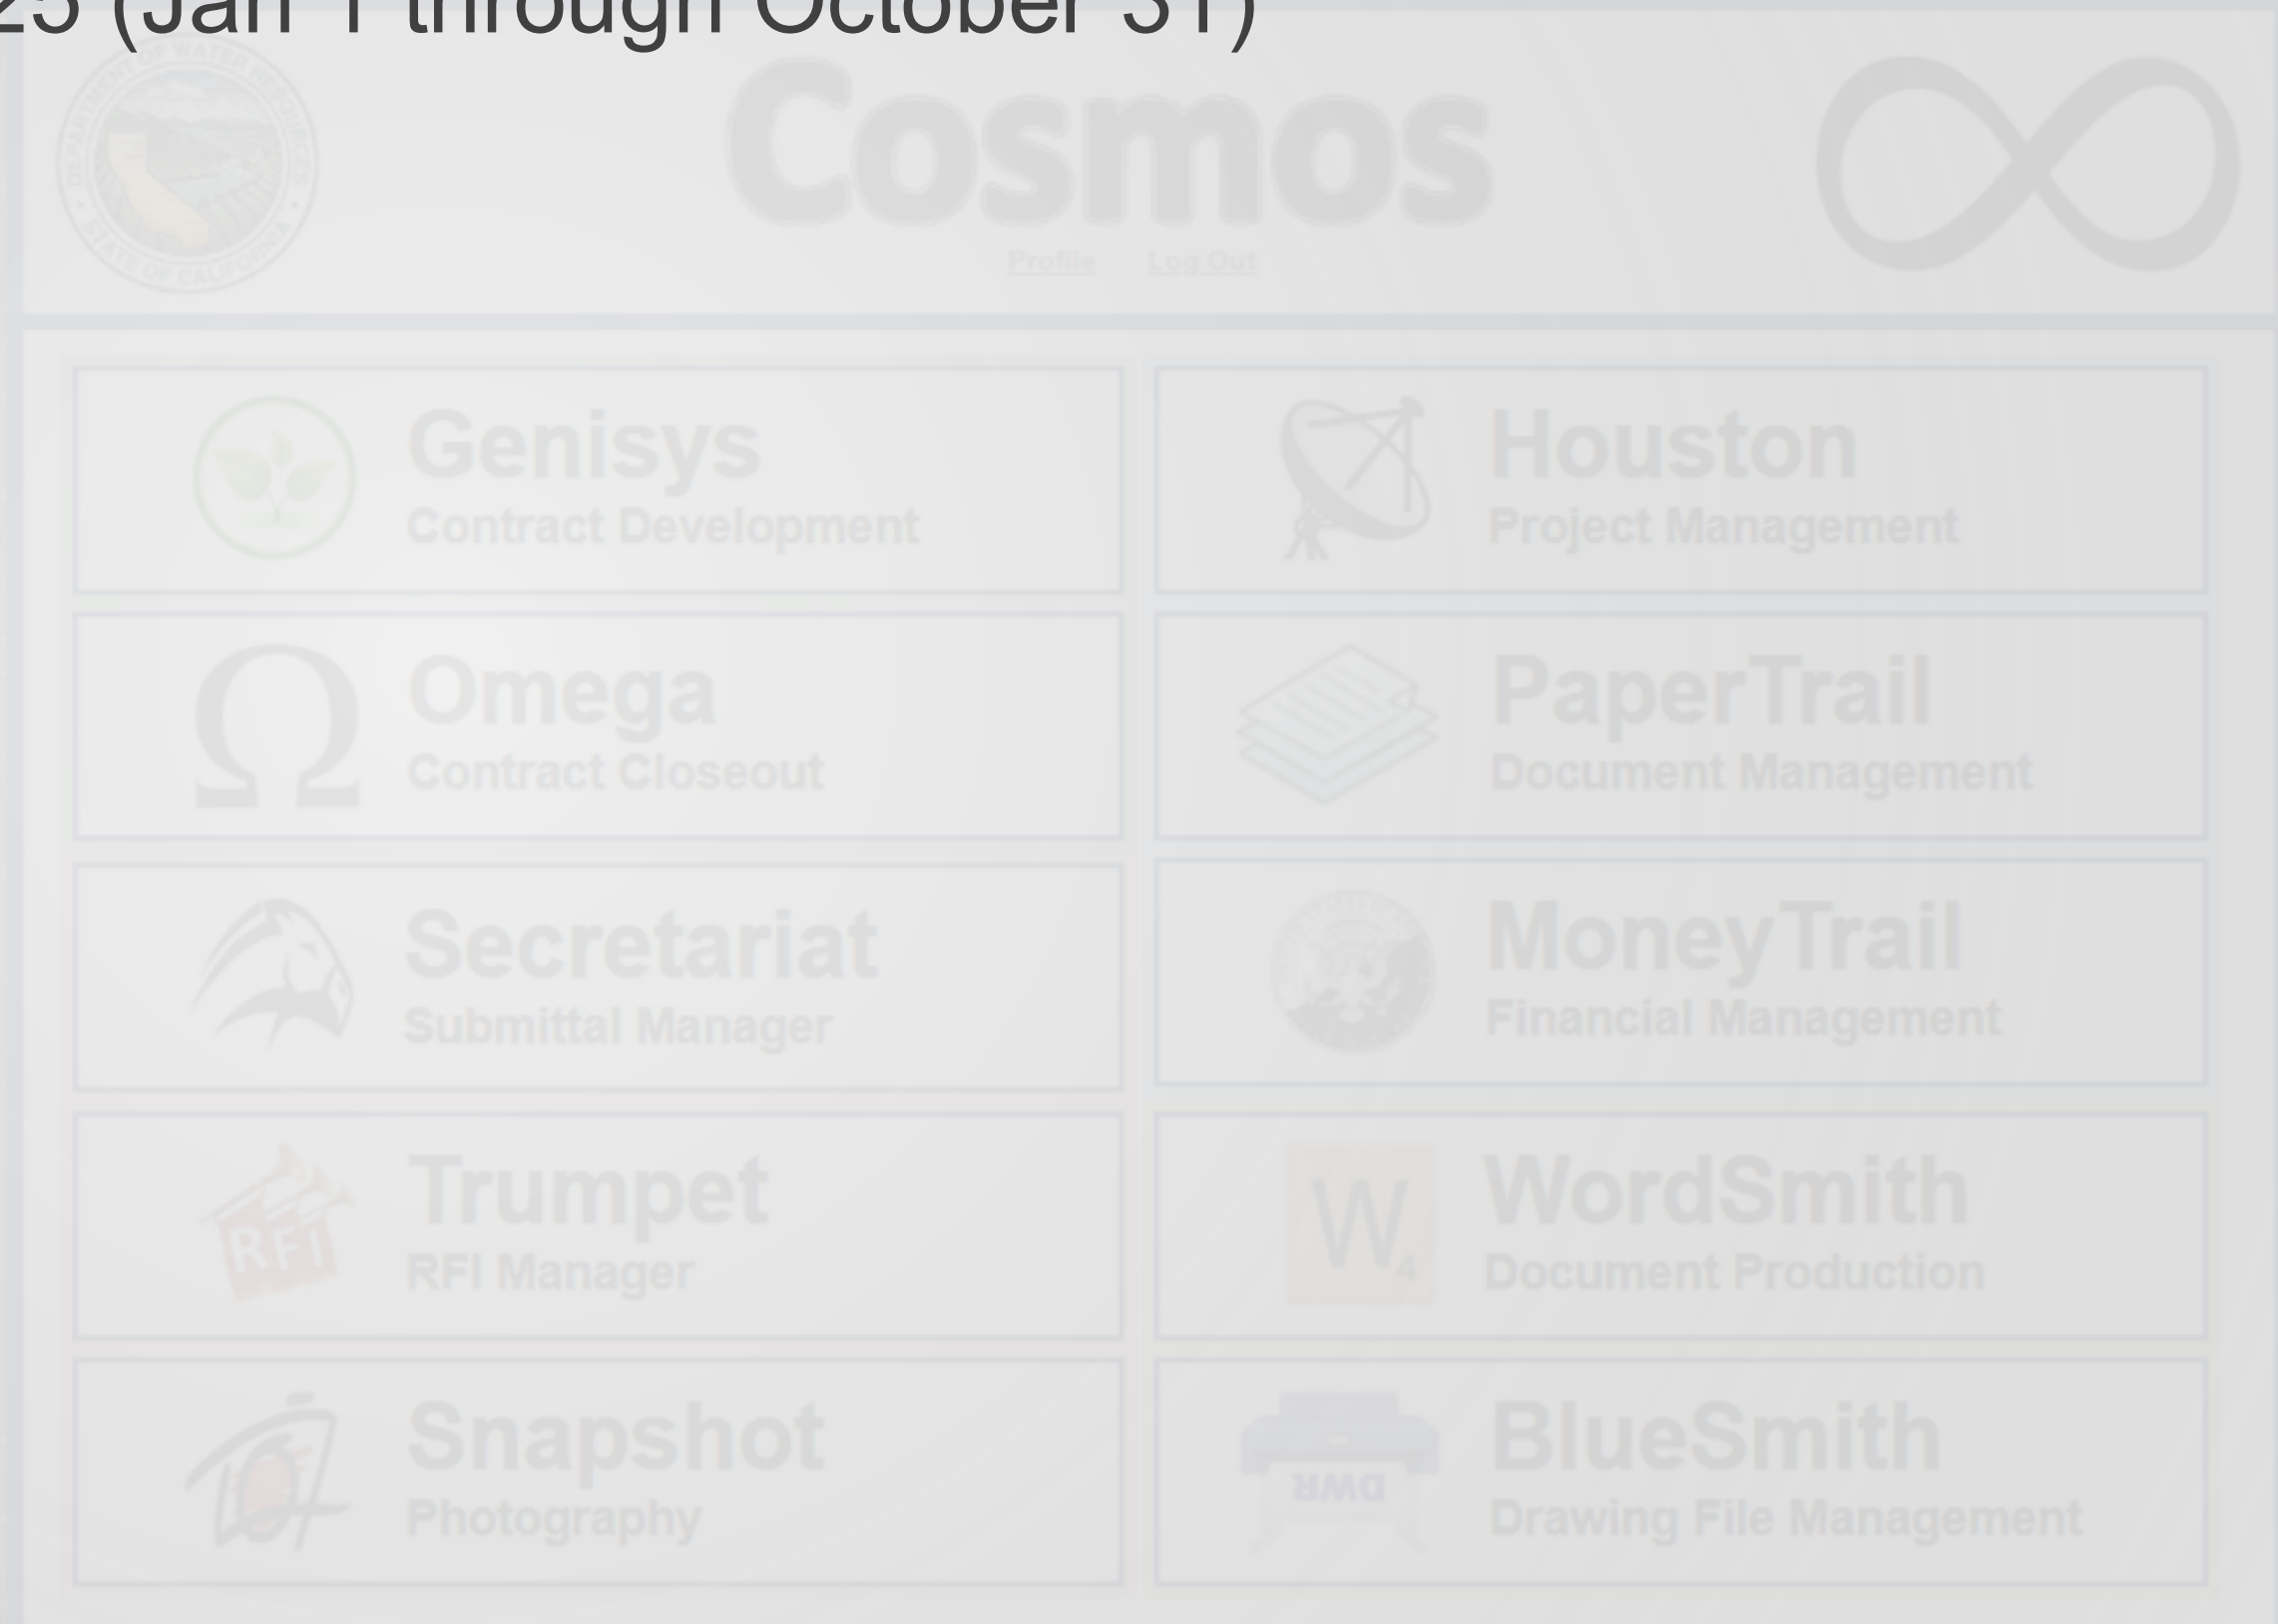

Construction Contracts

Completed in 2025, within
State Water Resources
Development System



Data Date: 11/5/2025
Contracts: 8
Total Amount: \$64.0M

Spec No	Contract Title	Contractor	Award Date	Current Contract	Percent Complete
22-02	River Valve Outlet System Rehabilitation, Oroville Dam Diversion Tunnel No. 2	Kiewit Infrastructure West Co.	5/18/2022	\$45,000,000	100.0%
22-03	Temporary Rock Barriers - 2022, 2023 and 2024, Middle River, Old River, and Grant Line Canal	Cal-Neva Construction Services, Inc.	4/1/2022	\$8,479,003	100.0%
22-06	Electric Vehicle Charging Station Infrastructure	Anderson Burton Construction, Inc.	10/31/2022	\$3,324,154	100.0%
23-17	Abandoned Pipes and Conduits Removal, Sacramento River	The Design Build, Inc.	4/25/2024	\$729,959	100.0%
24-01	Canal Improvements, Palermo Canal	NMN Construction, Inc	10/4/2024	\$348,975	100.0%
24-02	Roofing Replacement, Edmonston Pumping Plant	Best Contracting Services, Inc.	4/2/2024	\$1,569,505	100.0%
24-04	Roofing Replacement, Operations & Maintenance Center, Surveillance Unit & Vehicle Storage Buildings	D K Enterprises, Inc., dba King\'s Roofing	7/24/2024	\$768,854	100.0%
24-12	Chipps Island- Phase 2B North Parcel Interim Management and Levee Repairs	Dixon Marine Services, Inc.	7/19/2024	\$3,822,316	100.0%



Construction Contracts

Active in 2025, within
State Water Resources
Development System



Spec No	Contract Title	Contractor	Award Date	Current Contract	Percent Complete
21-05	Georgiana Slough Salmonid Migratory Barrier, Sacramento River	Cal-Neva Construction Services, Inc.	7/26/2021	\$19,127,359	99.9%
23-16	Roofing Replacement - 2023, O&M Center - Civil Maintenance Headquarters, O&M Center - Plant Maintenance Shops, Del Valle Pumping Plant, Byron and Livermore California	Andy\'s Roofing Co. Inc.	9/1/2023	\$1,945,475	99.9%
22-07	Repair of Fish Louver Supports, J.E. Skinner Fish Facility	DRS Marine Inc.	5/27/2022	\$1,316,046	99.1%
22-04	Salmonid Habitat Restoration and Fish Passage - Big Notch, Fremont Weir - Yolo Bypass	Goodfellow Bros. California, LLC	5/13/2022	\$45,599,570	96.8%
23-18	Seal and Pave Roads - 2023, San Luis Field Division	Granite Construction Company	9/19/2023	\$3,740,695	95.6%
20-03	Replacement of Radial Gates, Check Structures 3,4,6, and 9	NMI Industrial Holdings, Inc.	5/7/2021	\$4,953,047	95.5%
24-03	Rodent Burrow Remediation	K. W. Emerson, Inc.	4/15/2024	\$3,485,581	89.7%
22-08	Physical Security Upgrades (Central) - Phase I	Anderson Burton Construction, Inc.	4/3/2023	\$13,750,149	87.9%
25-02	River Valve Outlet System Rehabilitation, Oroville Dam Diversion Tunnel No. 2	Syblon Reid-Dutra JV	2/10/2025	\$38,628,574	85.9%
20-08	Radial Gates Refurbishment and Headworks Repair - Thermalito Afterbay	Gracon LLC	11/9/2020	\$12,533,180	84.4%
25-05	Chipps Island Tidal Habitat Restoration Project-Phase 2C	Dixon Marine Services, Inc.	4/3/2025	\$9,510,494	71.3%
24-09	Canal Liner and Embankment Repairs, MP 10.49 to MP 63.65 (California Aqueduct), MP 12.61 (South Bay Aqueduct)	Power Engineering Construction Co.	8/13/2024	\$1,811,618	70.4%
20-21	Canal Liner and Embankment Repairs, MP 303.41 To MP 403.41 (East Branch), MP 0.00 To MP 8.25 (West Branch)	R. C. Becker & Son, Inc.	11/23/2020	\$2,417,788	70.3%



Construction Contracts

Active in 2025, within
State Water Resources
Development System



Data Date: 11/5/2025

Contracts: 26

Total Amount: \$366.8M



CALIFORNIA DEPARTMENT OF
WATER RESOURCES



Spec No	Contract Title	Contractor	Award Date	Current Contract	Percent Complete
23-04	Spillway Maintenance, Cedar Springs Dam and Pyramid Dam	Syblon Reid	6/14/2023	\$3,455,366	68.7%
23-15	Maintenance Repairs, Oroville Dam Flood Control Outlet Spillway	Syblon Reid	7/28/2023	\$8,070,731	68.0%
20-07	Fire Safety Modernization, Gianelli Pumping-Generating Plant, SLFD O&M Center, Dos Amigos PP, and Coalinga O&M Center	Thompson Builders Corporation	9/21/2023	\$100,978,740	61.9%
21-06	Canal Liner Repairs, MP 172.44 To MP 294.93 (California Aqueduct), MP 0.00 To MP 14.82 (Coastal Branch)	Bosco Constructors, Inc.	9/3/2021	\$3,038,956	59.0%
24-08	Physical Security Upgrades (South) - SFD - Phase I, Southern Field Division O&M Center, Pearblossom Pumping Plant, Oso Pumping Plant	Bowe Contractors Inc.	8/29/2024	\$7,354,334	57.7%
25-08	Seal and Pave Roads, Oroville-Thermalito Complex	Vintage Paving Co., Inc	7/6/2025	\$1,914,227	32.1%
22-09	Emergency Release Facility, Lake Perris	Sukut Construction, LLC	9/19/2024	\$61,328,052	24.2%
25-01	Temporary Rock Barriers - 2025, 2026, 2027, Middle River, Old River and Grant Line Canal	Cal-Neva Construction Services, Inc.	4/4/2025	\$7,994,622	18.7%
22-05	Well Replacement, Phase II, Thermalito Afterbay Dam	Syblon Reid	4/26/2024	\$4,998,301	18.4%
23-09	East and West Elevators Replacement	James E. Thompson, Inc. dba JTS Construction	4/23/2024	\$5,142,250	4.80%
25-07	Georgiana Slough Salmonid Migratory Barrier - 2025, 2026 and 2027	Cal-Neva Construction Services, Inc.	7/7/2025	\$2,947,000	0.0%
25-10	Agricultural Road Crossing 1 and Tule Channel - Site Preparation, Northern Yolo Bypass	Hanford Applied Restoration & Conservation	9/30/2025	\$368,650	0.0%
25-11	Agricultural Road Crossing No. 4 (ARC4) - Soil Surcharge	Nordic Industries, Inc.	9/30/2025	\$418,880	0.0%

Replacement of Radial Gates, Check Structures 3, 4, 6, and 9



CALIFORNIA DEPARTMENT OF
WATER RESOURCES





Replacement of Radial Gates, Check Structures 3, 4, 6, and 9




Replacement of Radial Gates, Check Structures 3, 4, 6, and 9



Replacement of Radial Gates, Check Structures 3, 4, 6, and 9



Replacement of Radial Gates, Check Structures 3, 4, 6, and 9

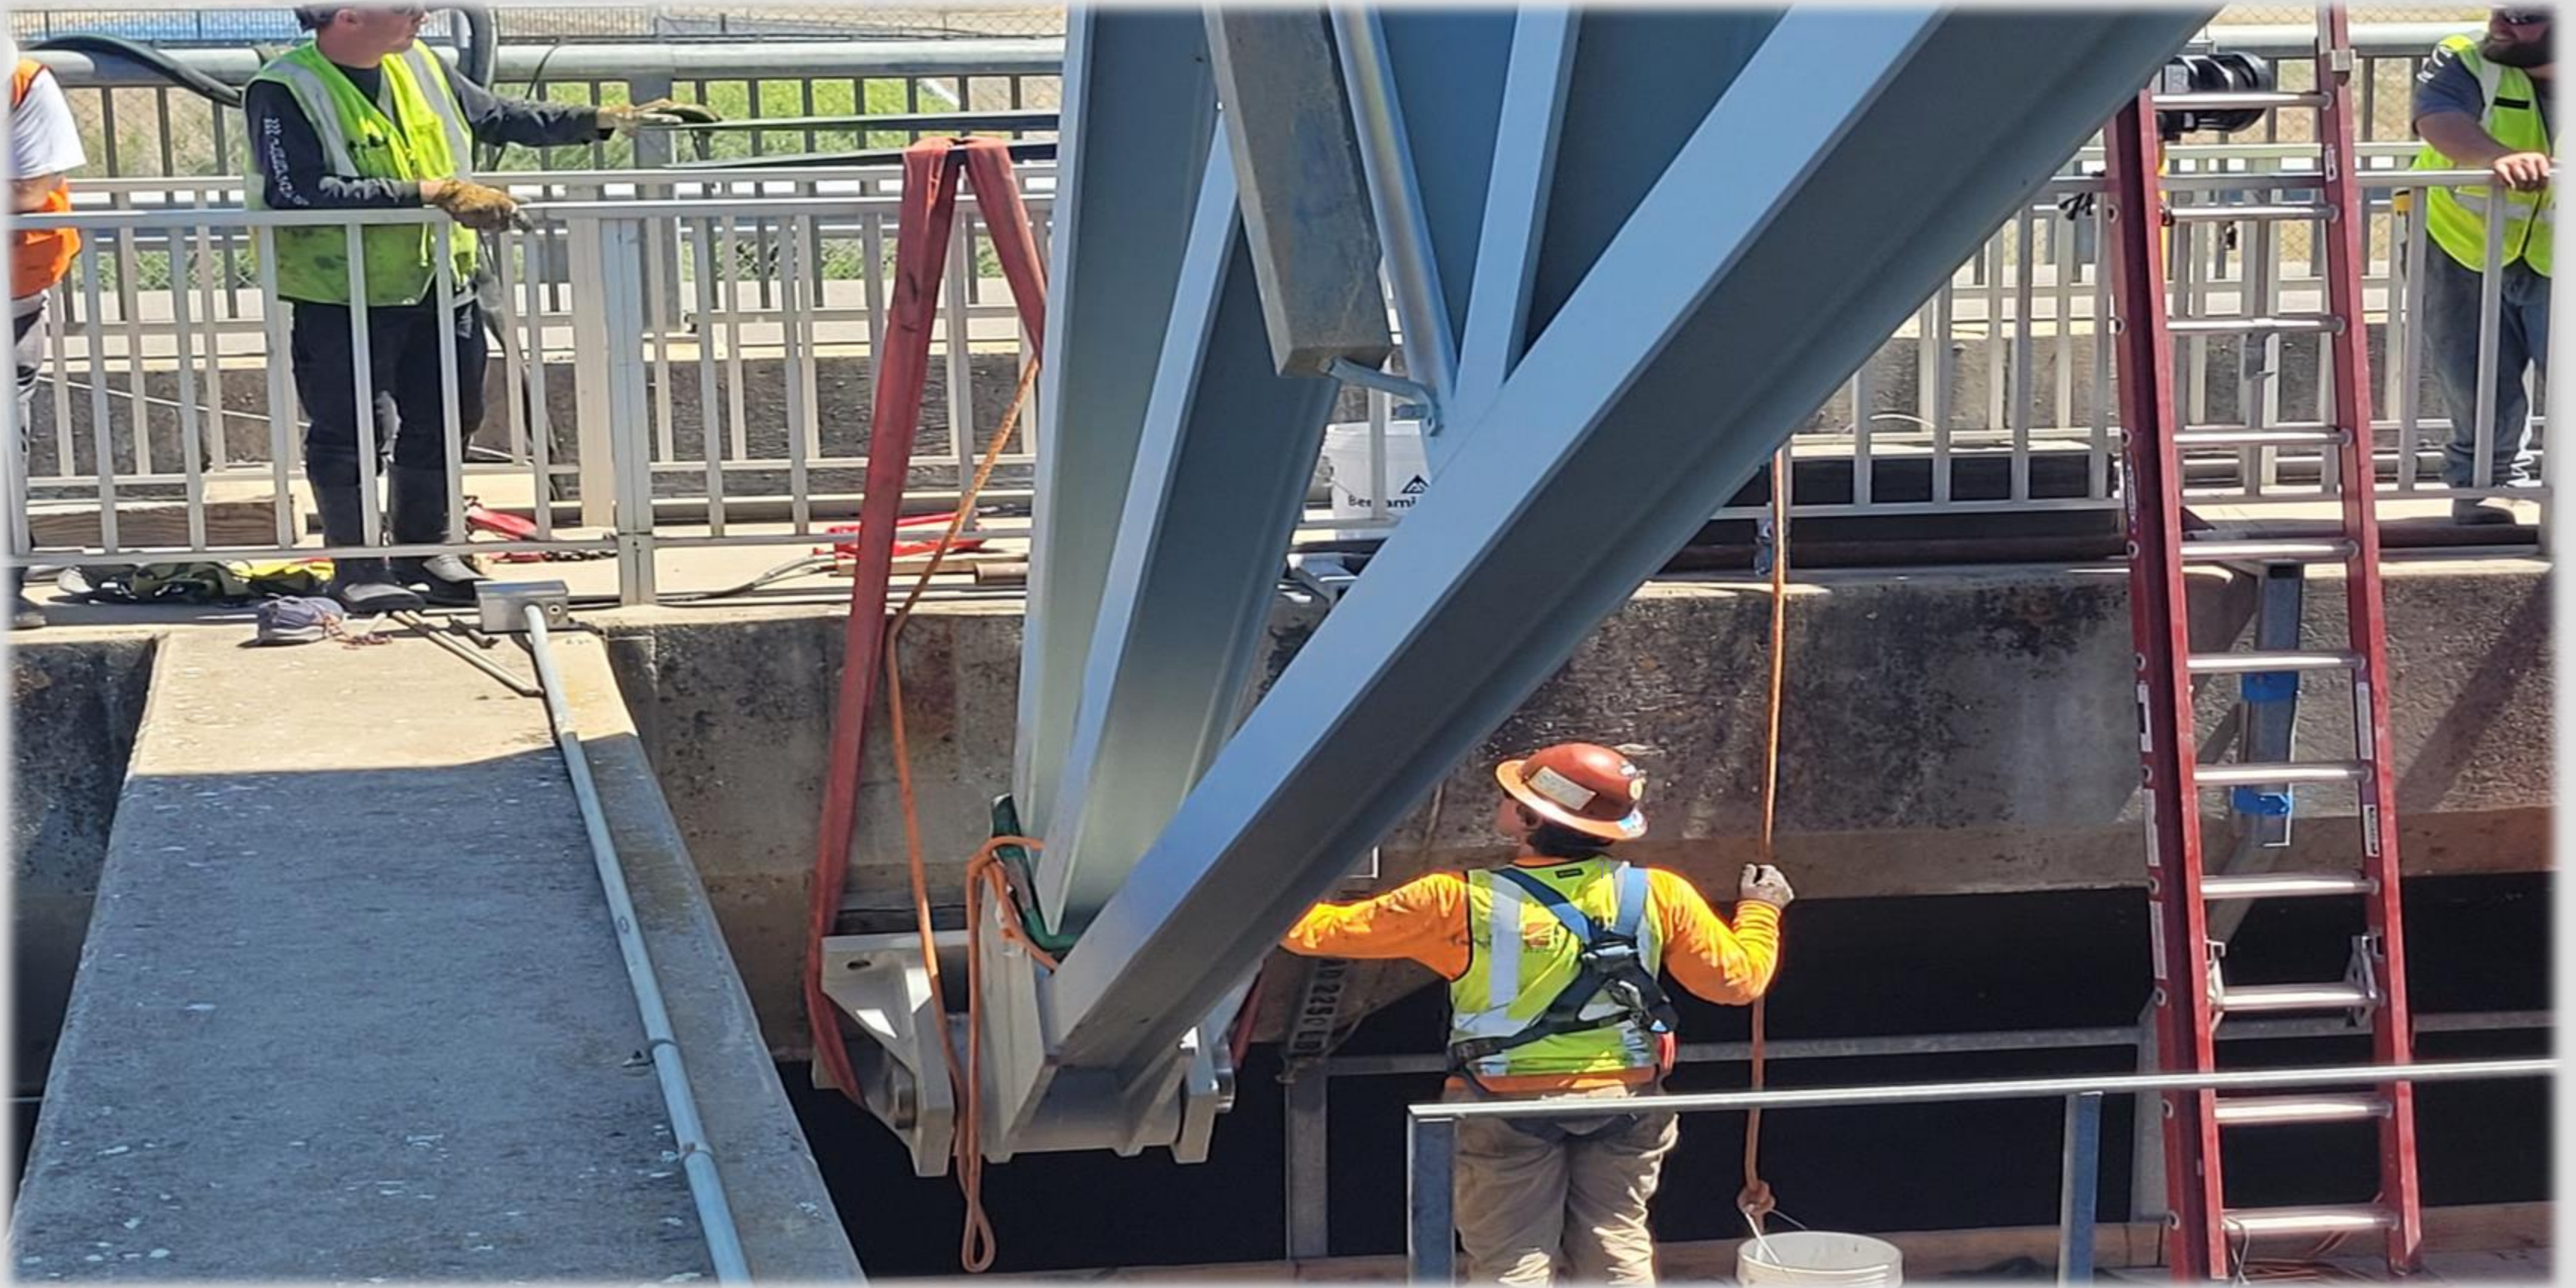



Replacement of Radial Gates, Check Structures 3, 4, 6, and 9



Replacement of Radial Gates, Check Structures 3, 4, 6, and 9

River Valve Outlet System Rehabilitation

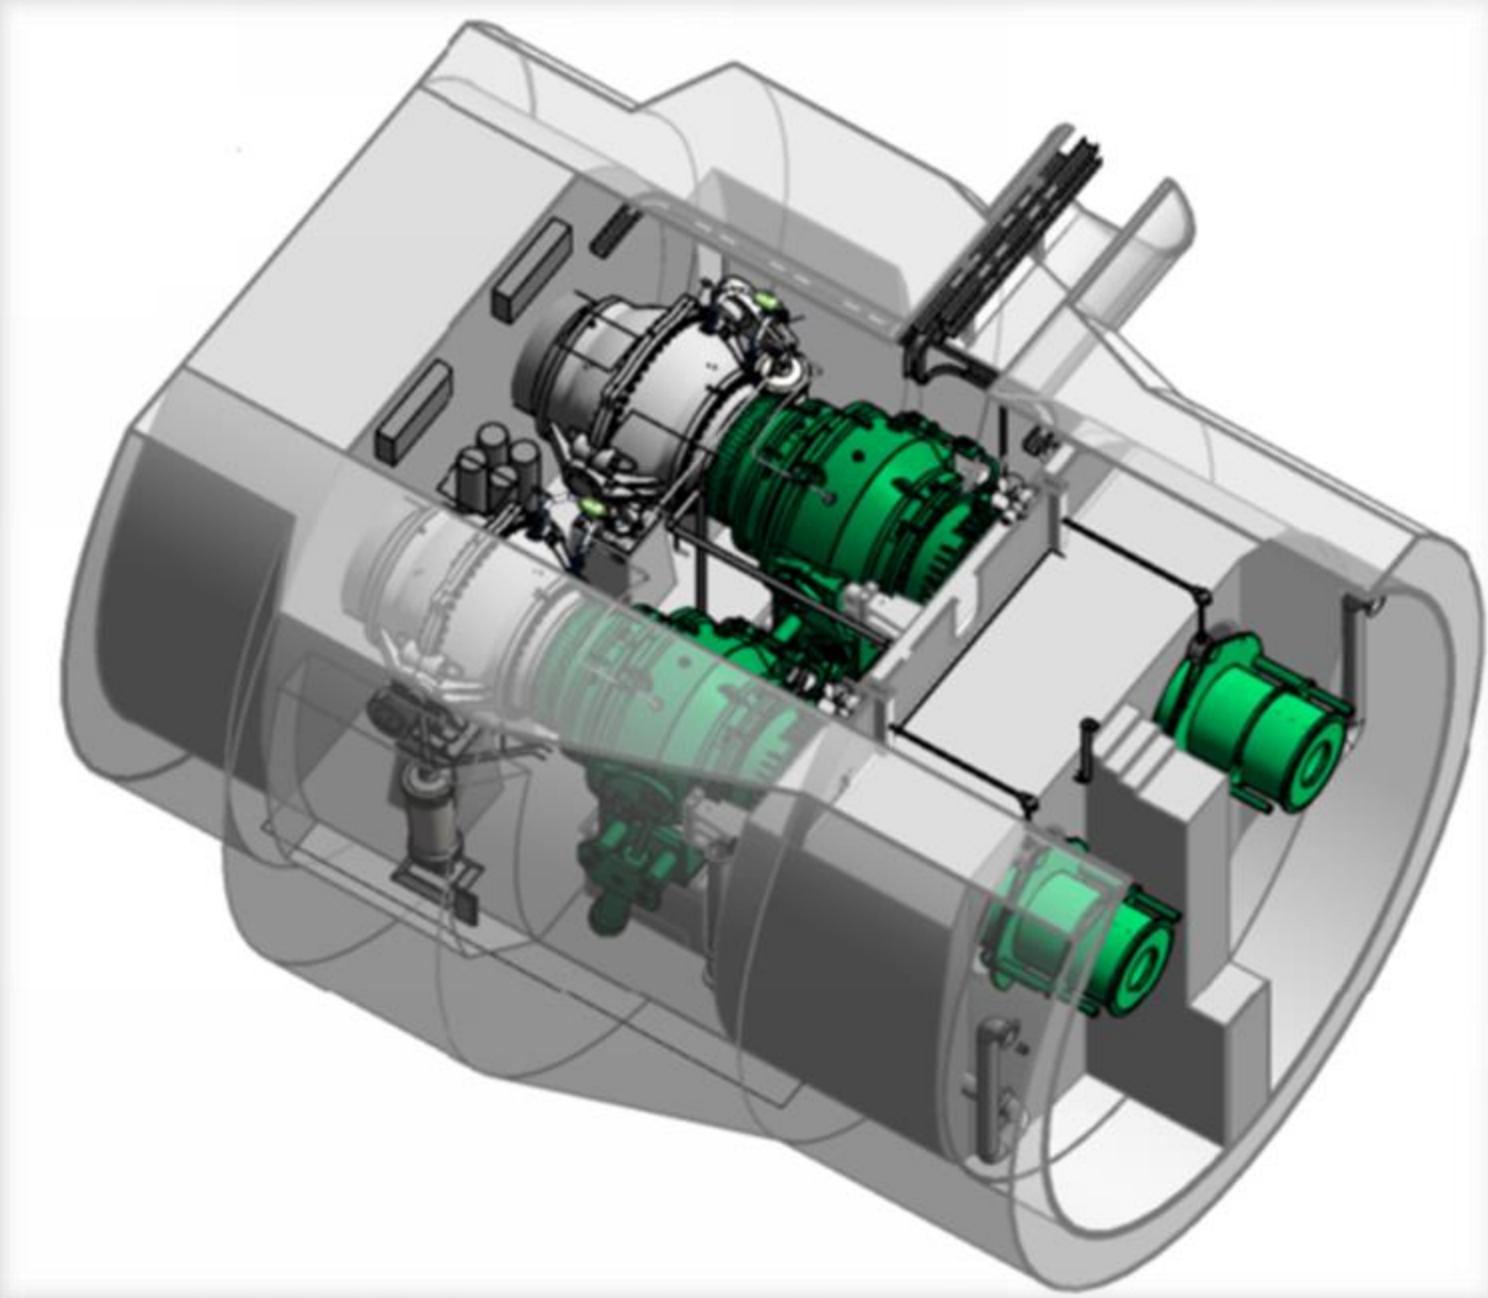

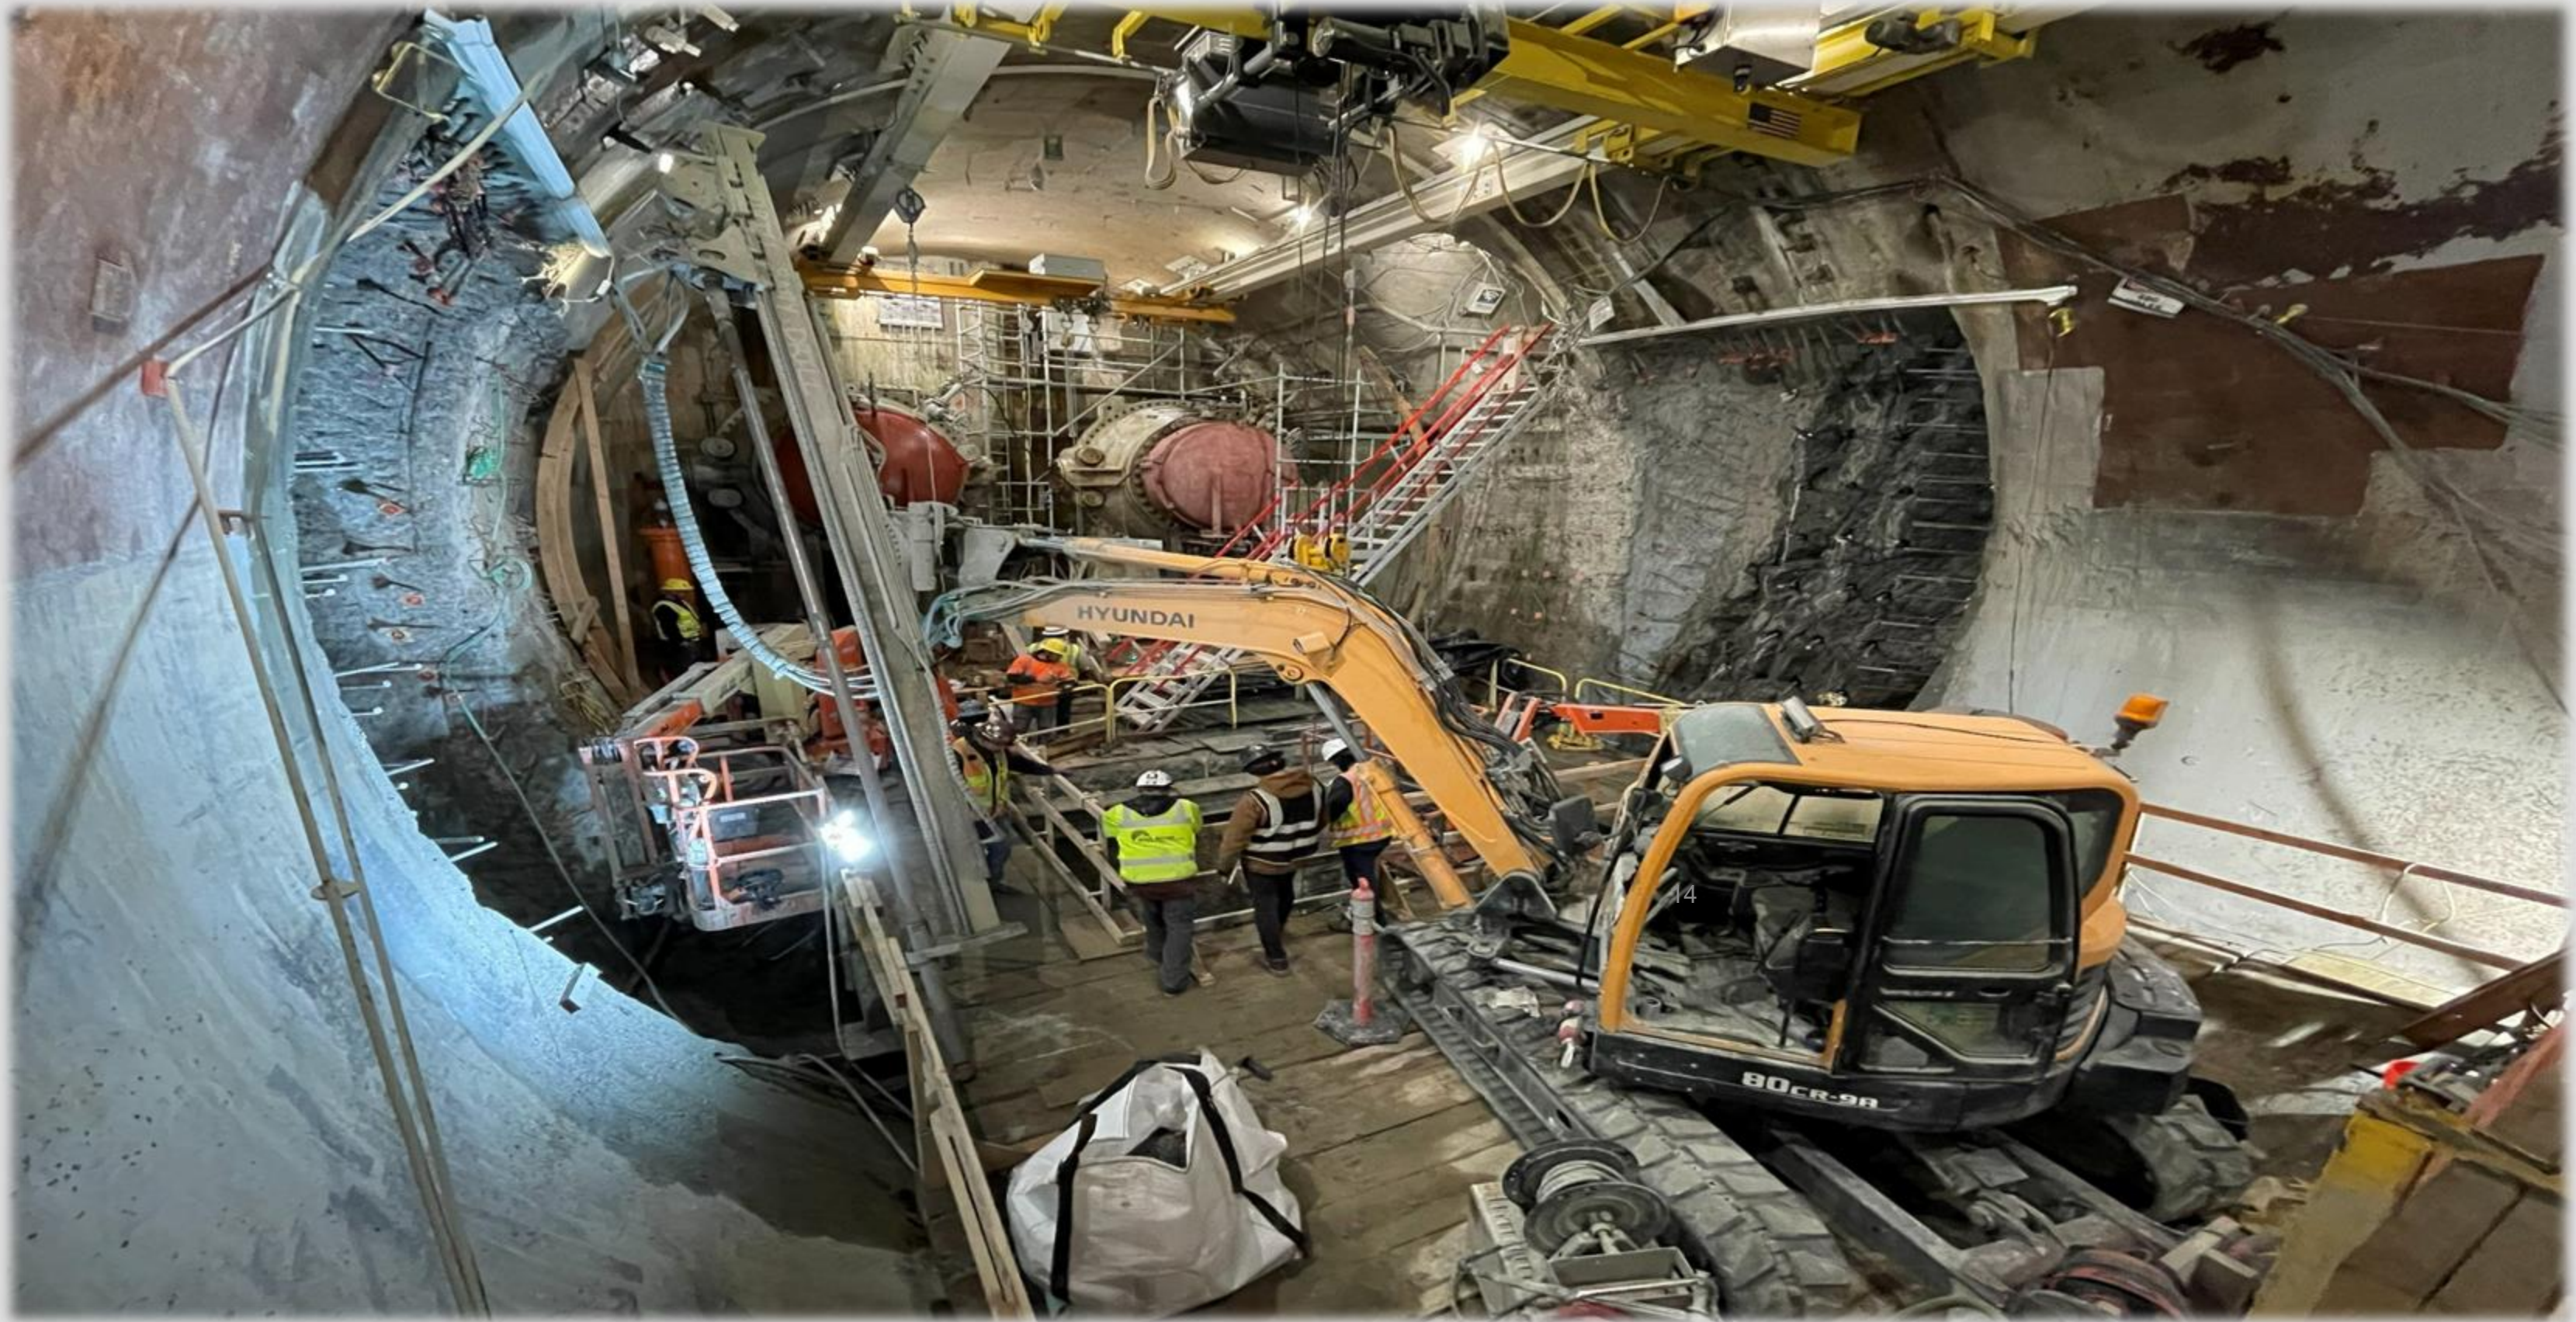


River Valve Outlet System Rehabilitation, Oroville Dam Diversion Tunnel No. 2



River Valve Outlet System Rehabilitation, Oroville Dam Diversion Tunnel No. 2



River Valve Outlet System Rehabilitation, Oroville Dam Diversion Tunnel No. 2

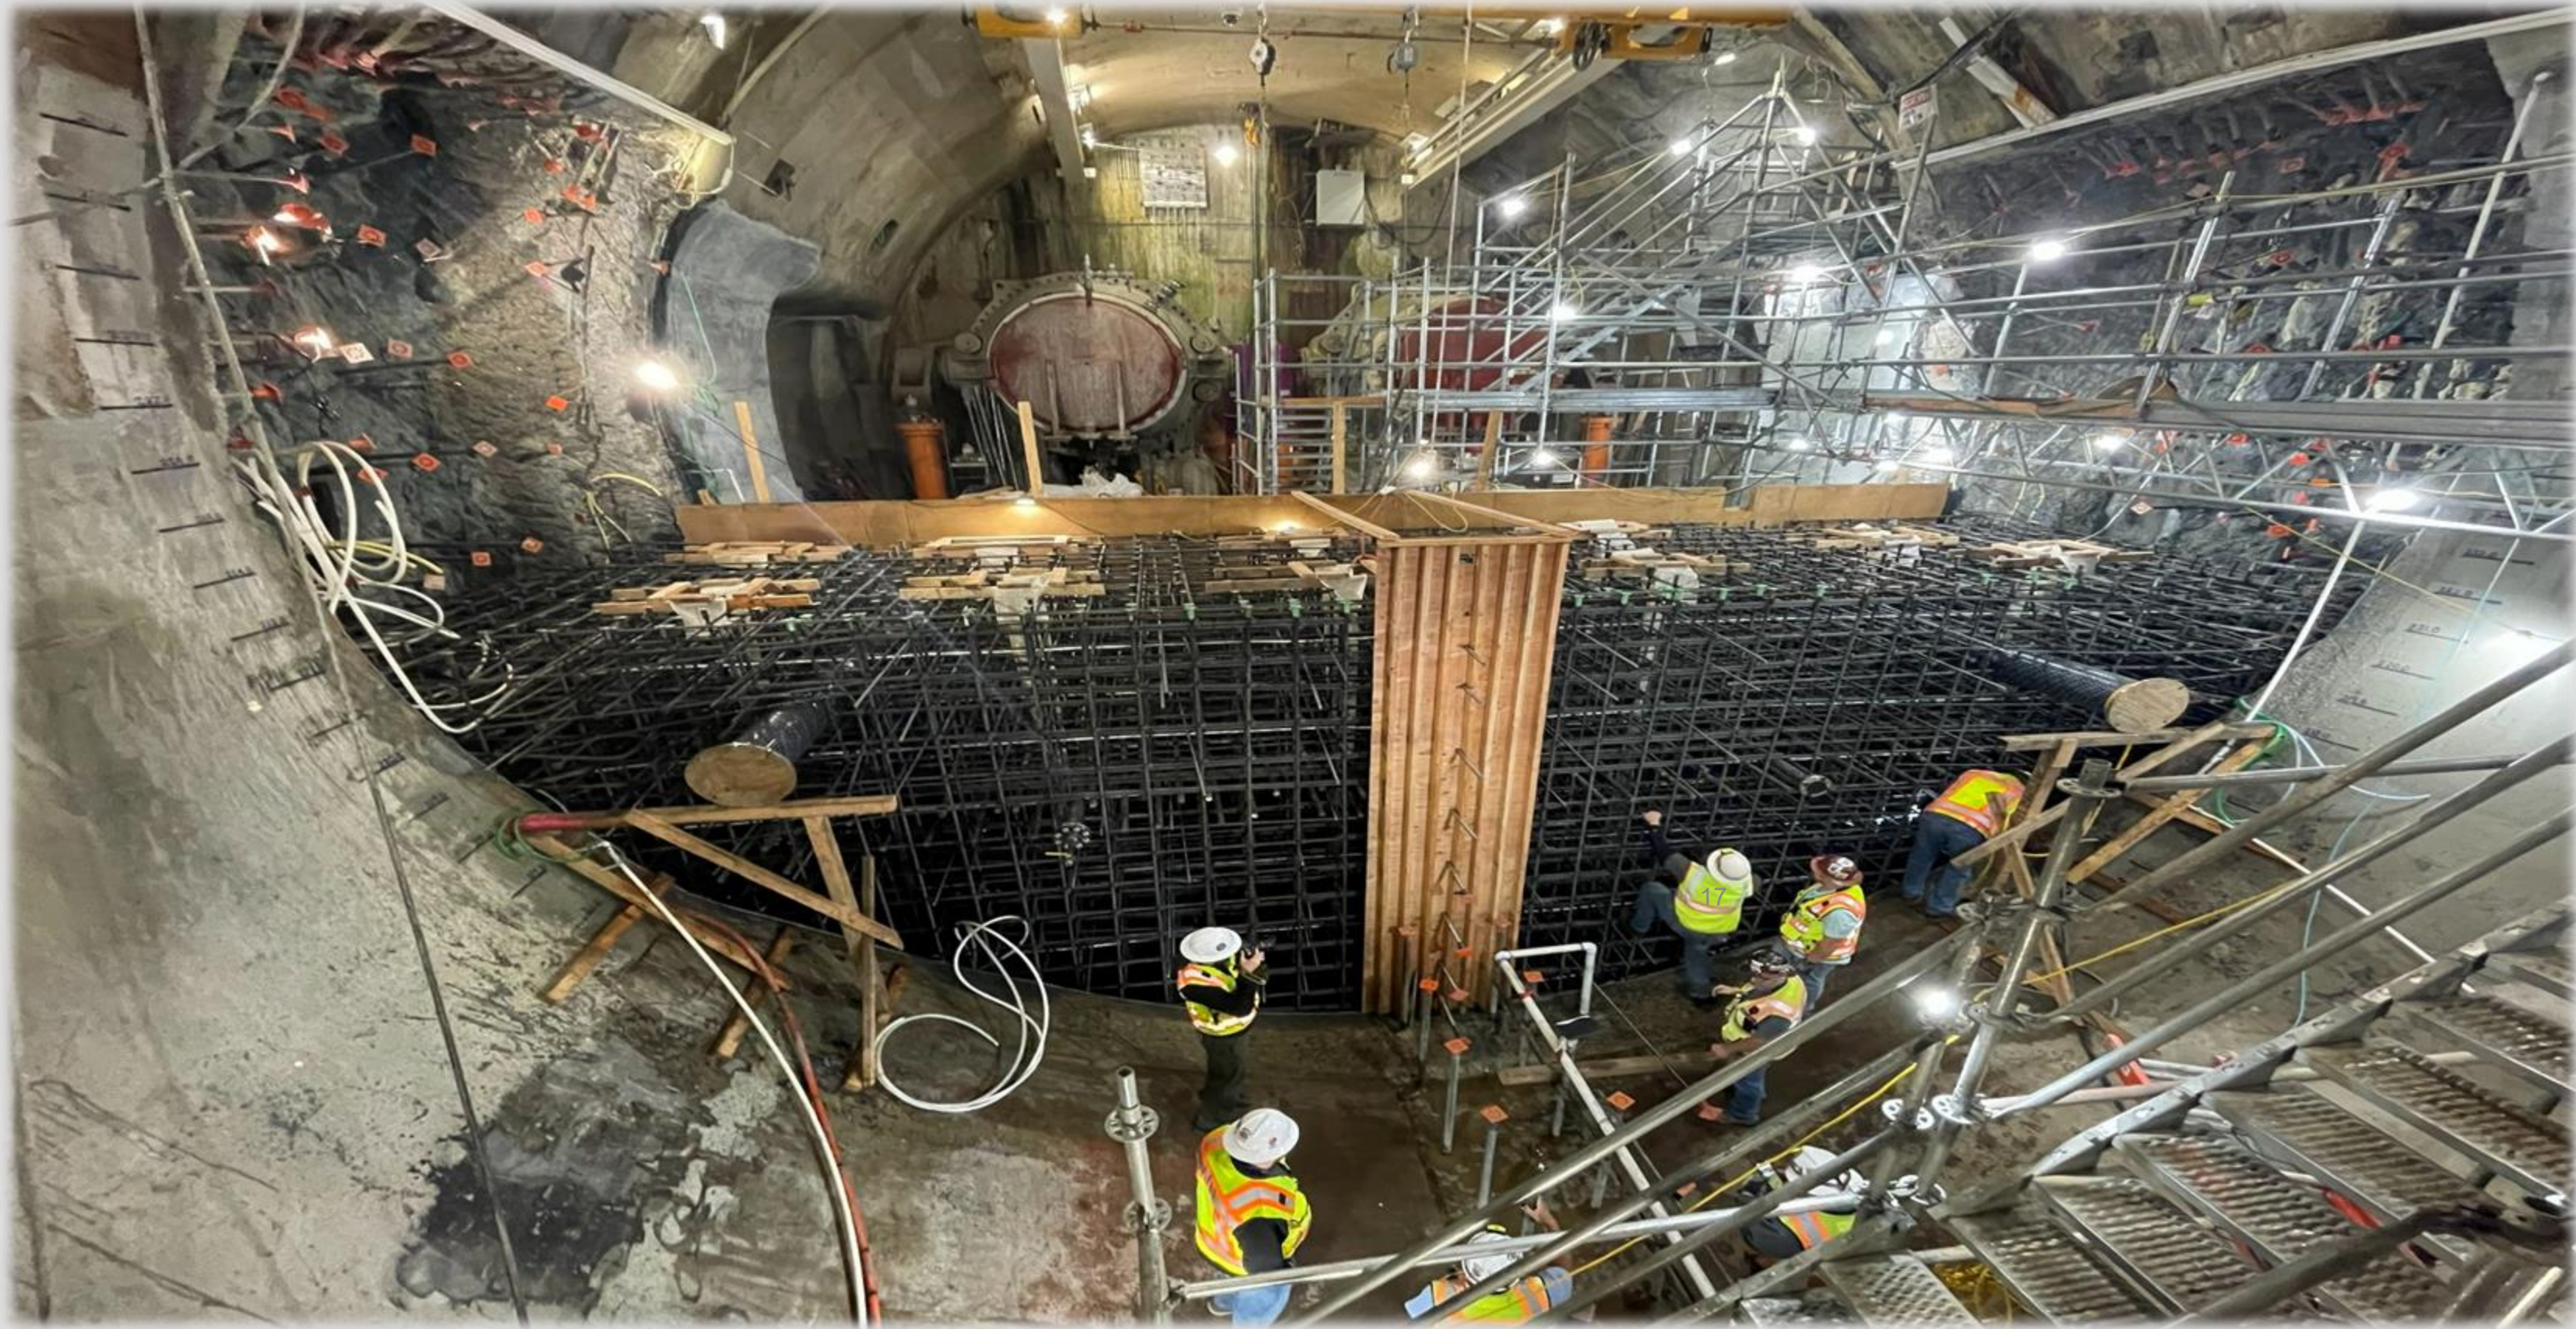


River Valve Outlet System Rehabilitation, Oroville Dam Diversion Tunnel No. 2



River Valve Outlet System Rehabilitation, Oroville Dam Diversion Tunnel No. 2



River Valve Outlet System Rehabilitation, Oroville Dam Diversion Tunnel No. 2

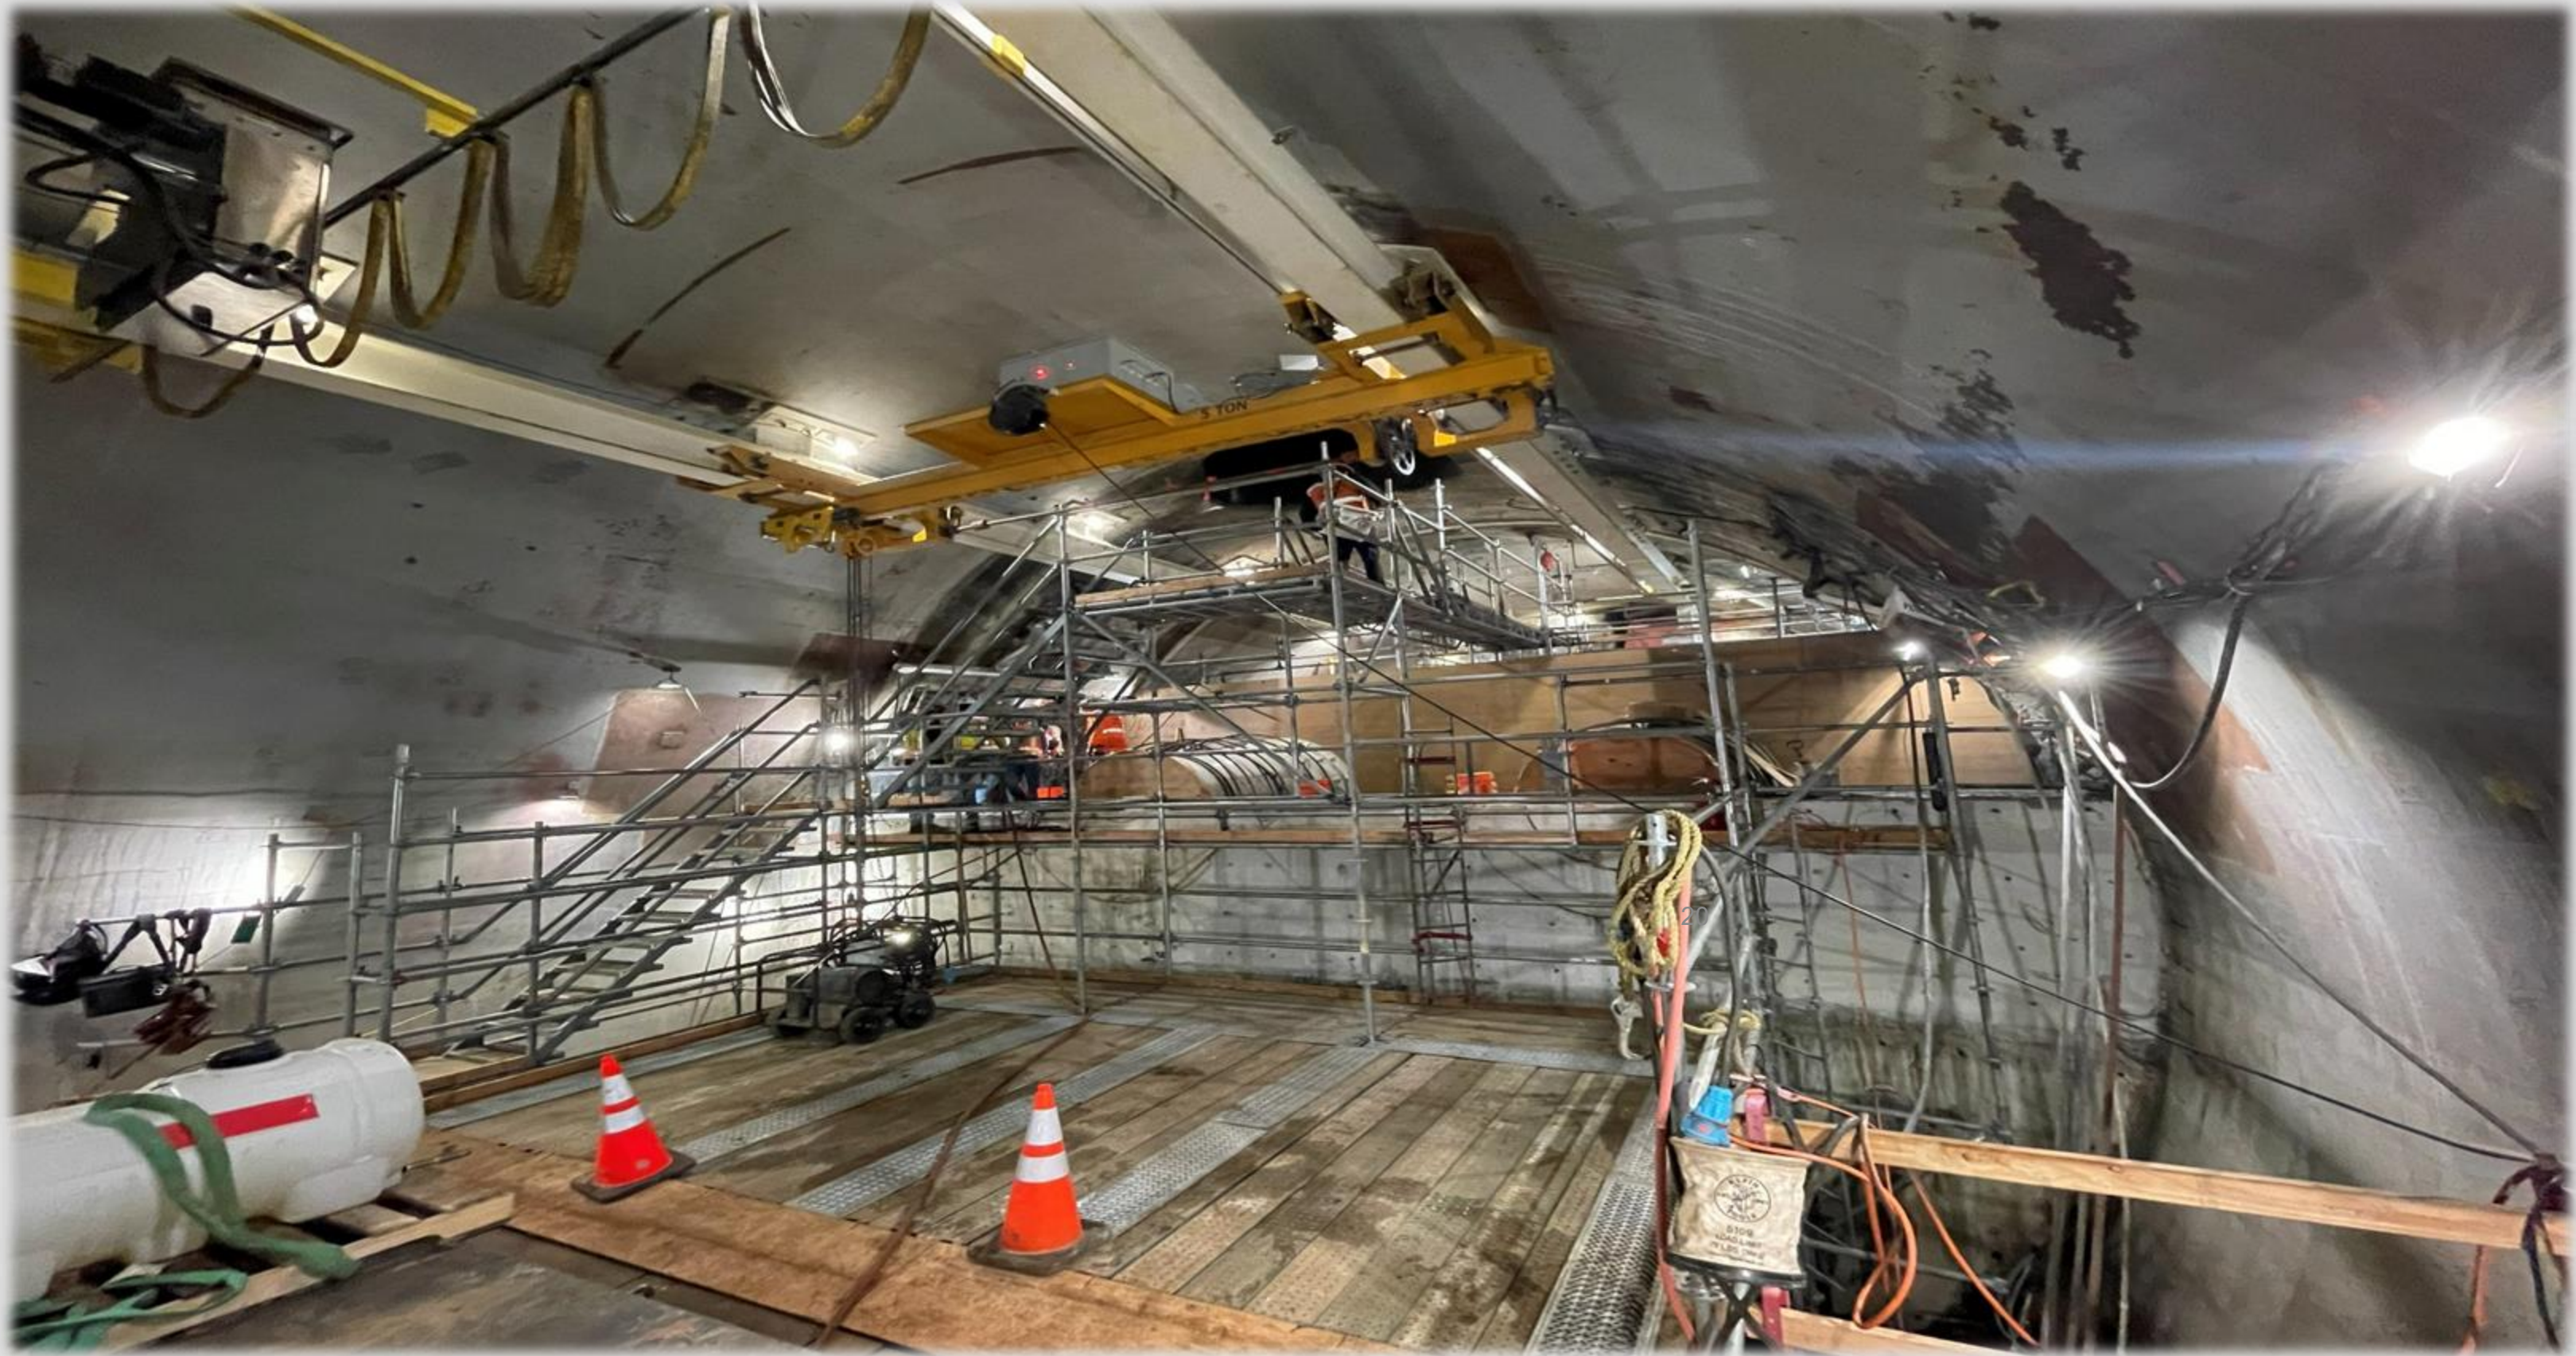

River Valve Outlet System Rehabilitation, Oroville Dam Diversion Tunnel No. 2

Fire Safety Modernization

Gianelli P/G Plant, SLFD O&M Center, Dos Amigos PP, and Coalinga O&M Center



CALIFORNIA DEPARTMENT OF
WATER RESOURCES






Fire Safety Modernization,
Gianelli P/G Plant, SLFD O&M Center, Dos Amigos PP, and Coalinga O&M Center



Fire Safety Modernization,
Gianelli P/G Plant, SLFD O&M Center, Dos Amigos PP, and Coalinga O&M Center




Fire Safety Modernization,
Gianelli P/G Plant, SLFD O&M Center, Dos Amigos PP, and Coalinga O&M Center

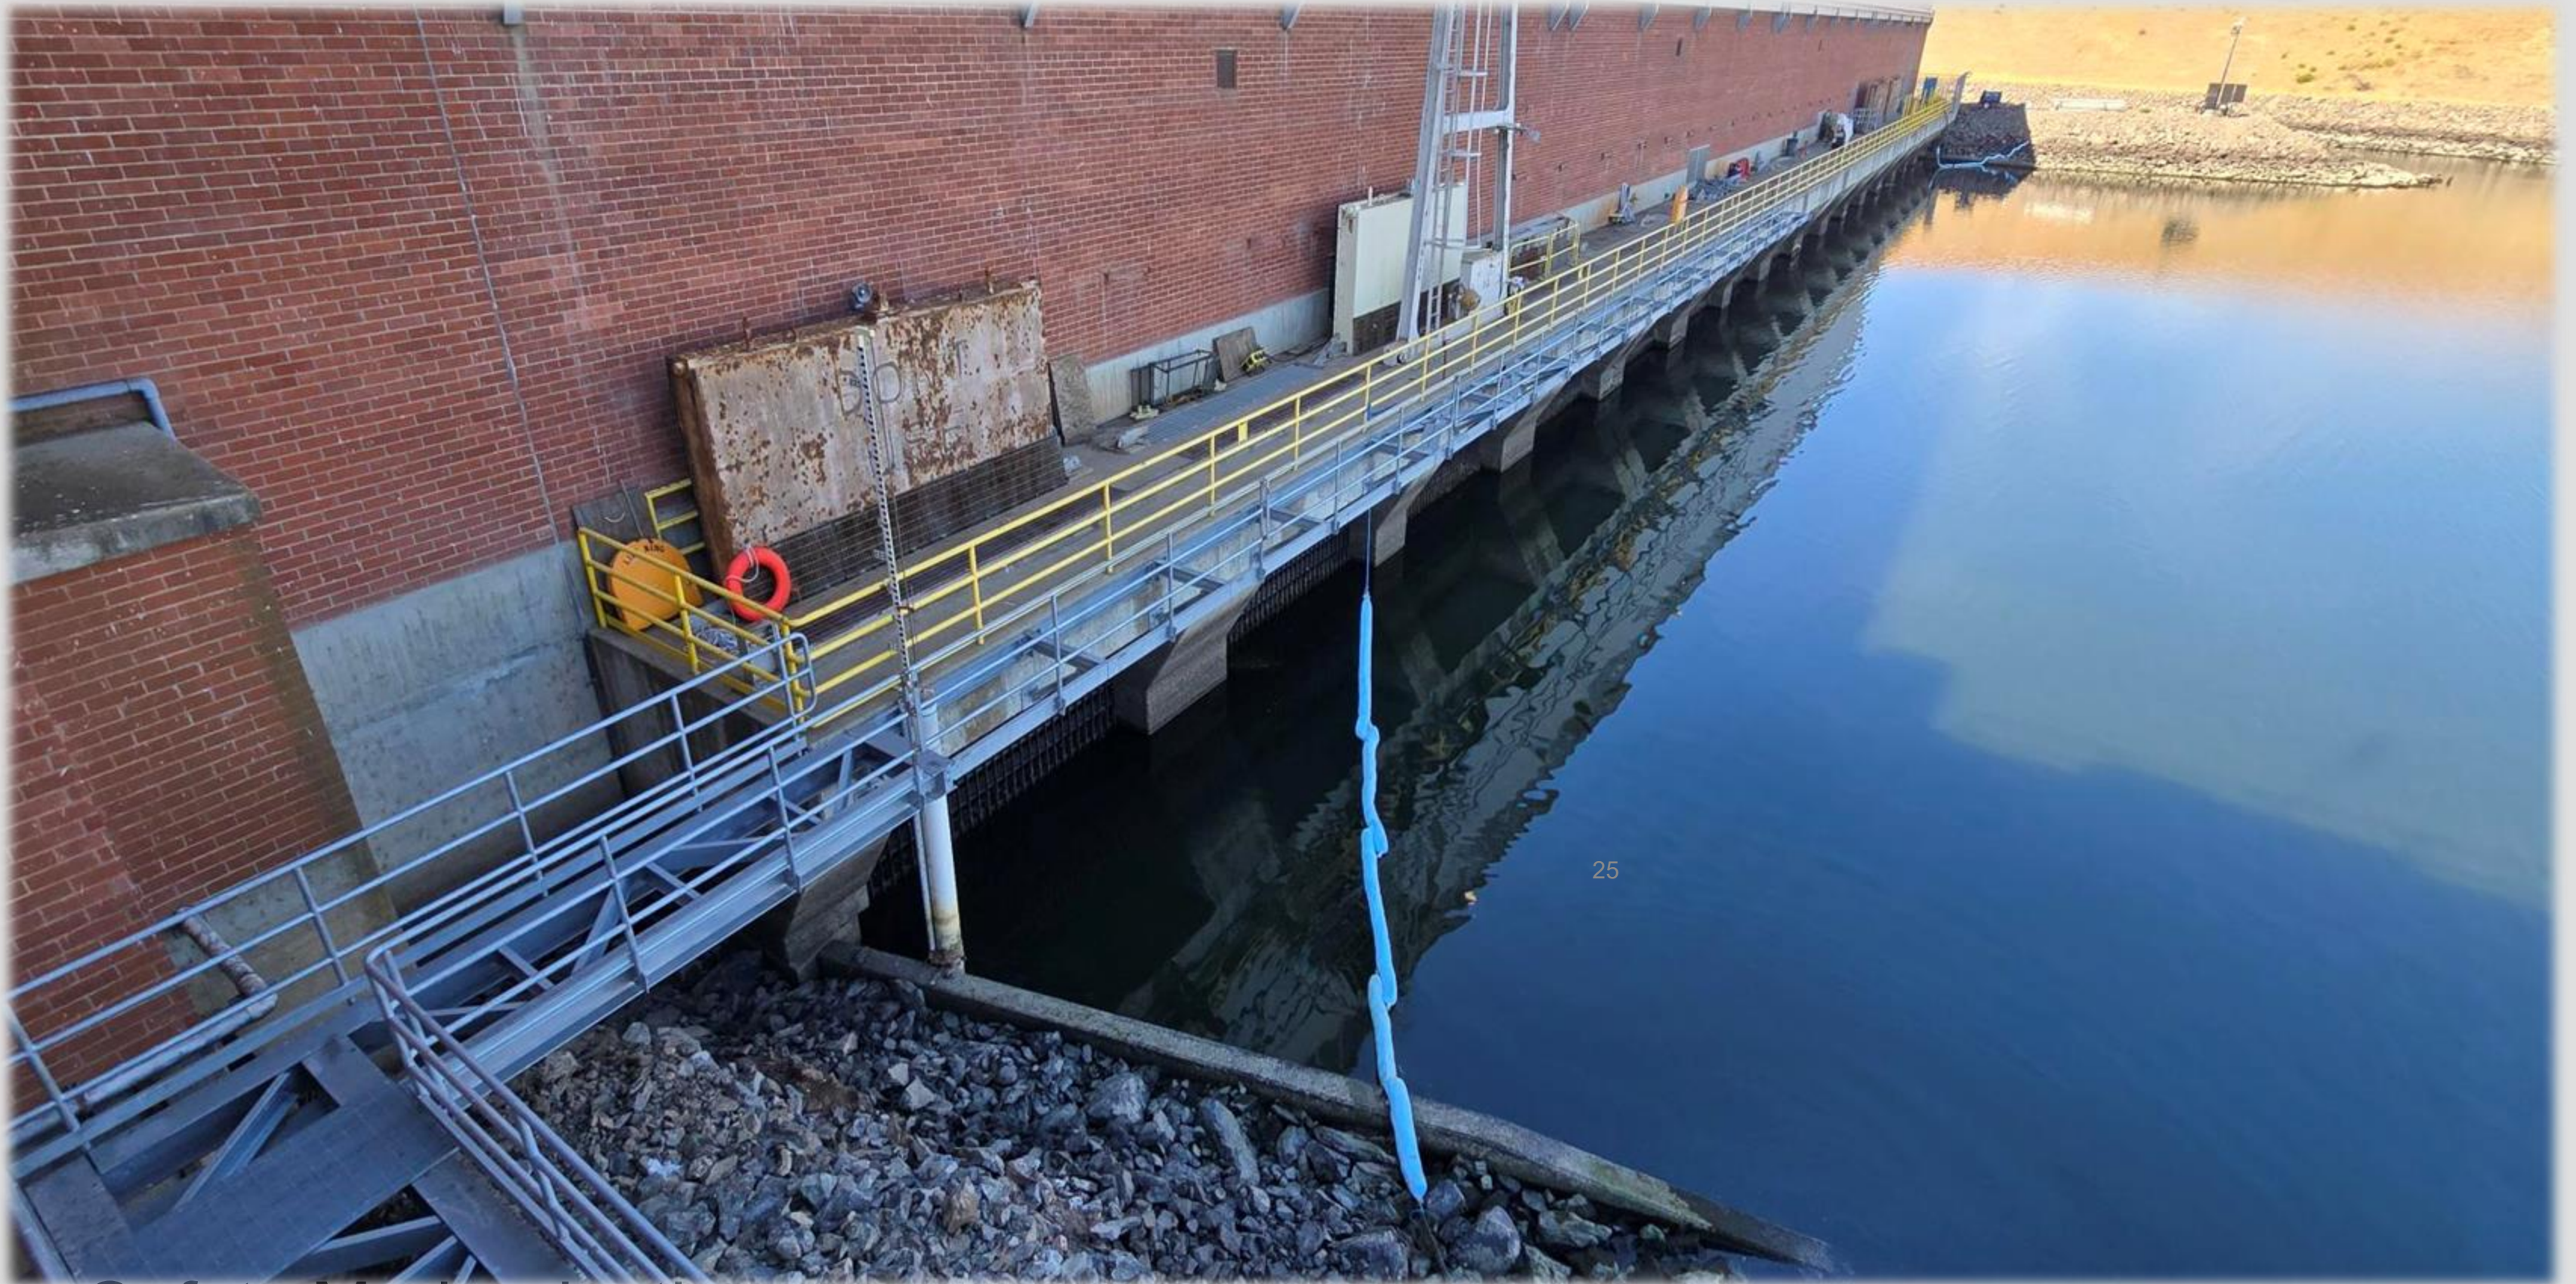

Fire Safety Modernization,
Gianelli P/G Plant, SLFD O&M Center, Dos Amigos PP, and Coalinga O&M Center



Fire Safety Modernization,
Gianelli P/G Plant, SLFD O&M Center, Dos Amigos PP, and Coalinga O&M Center

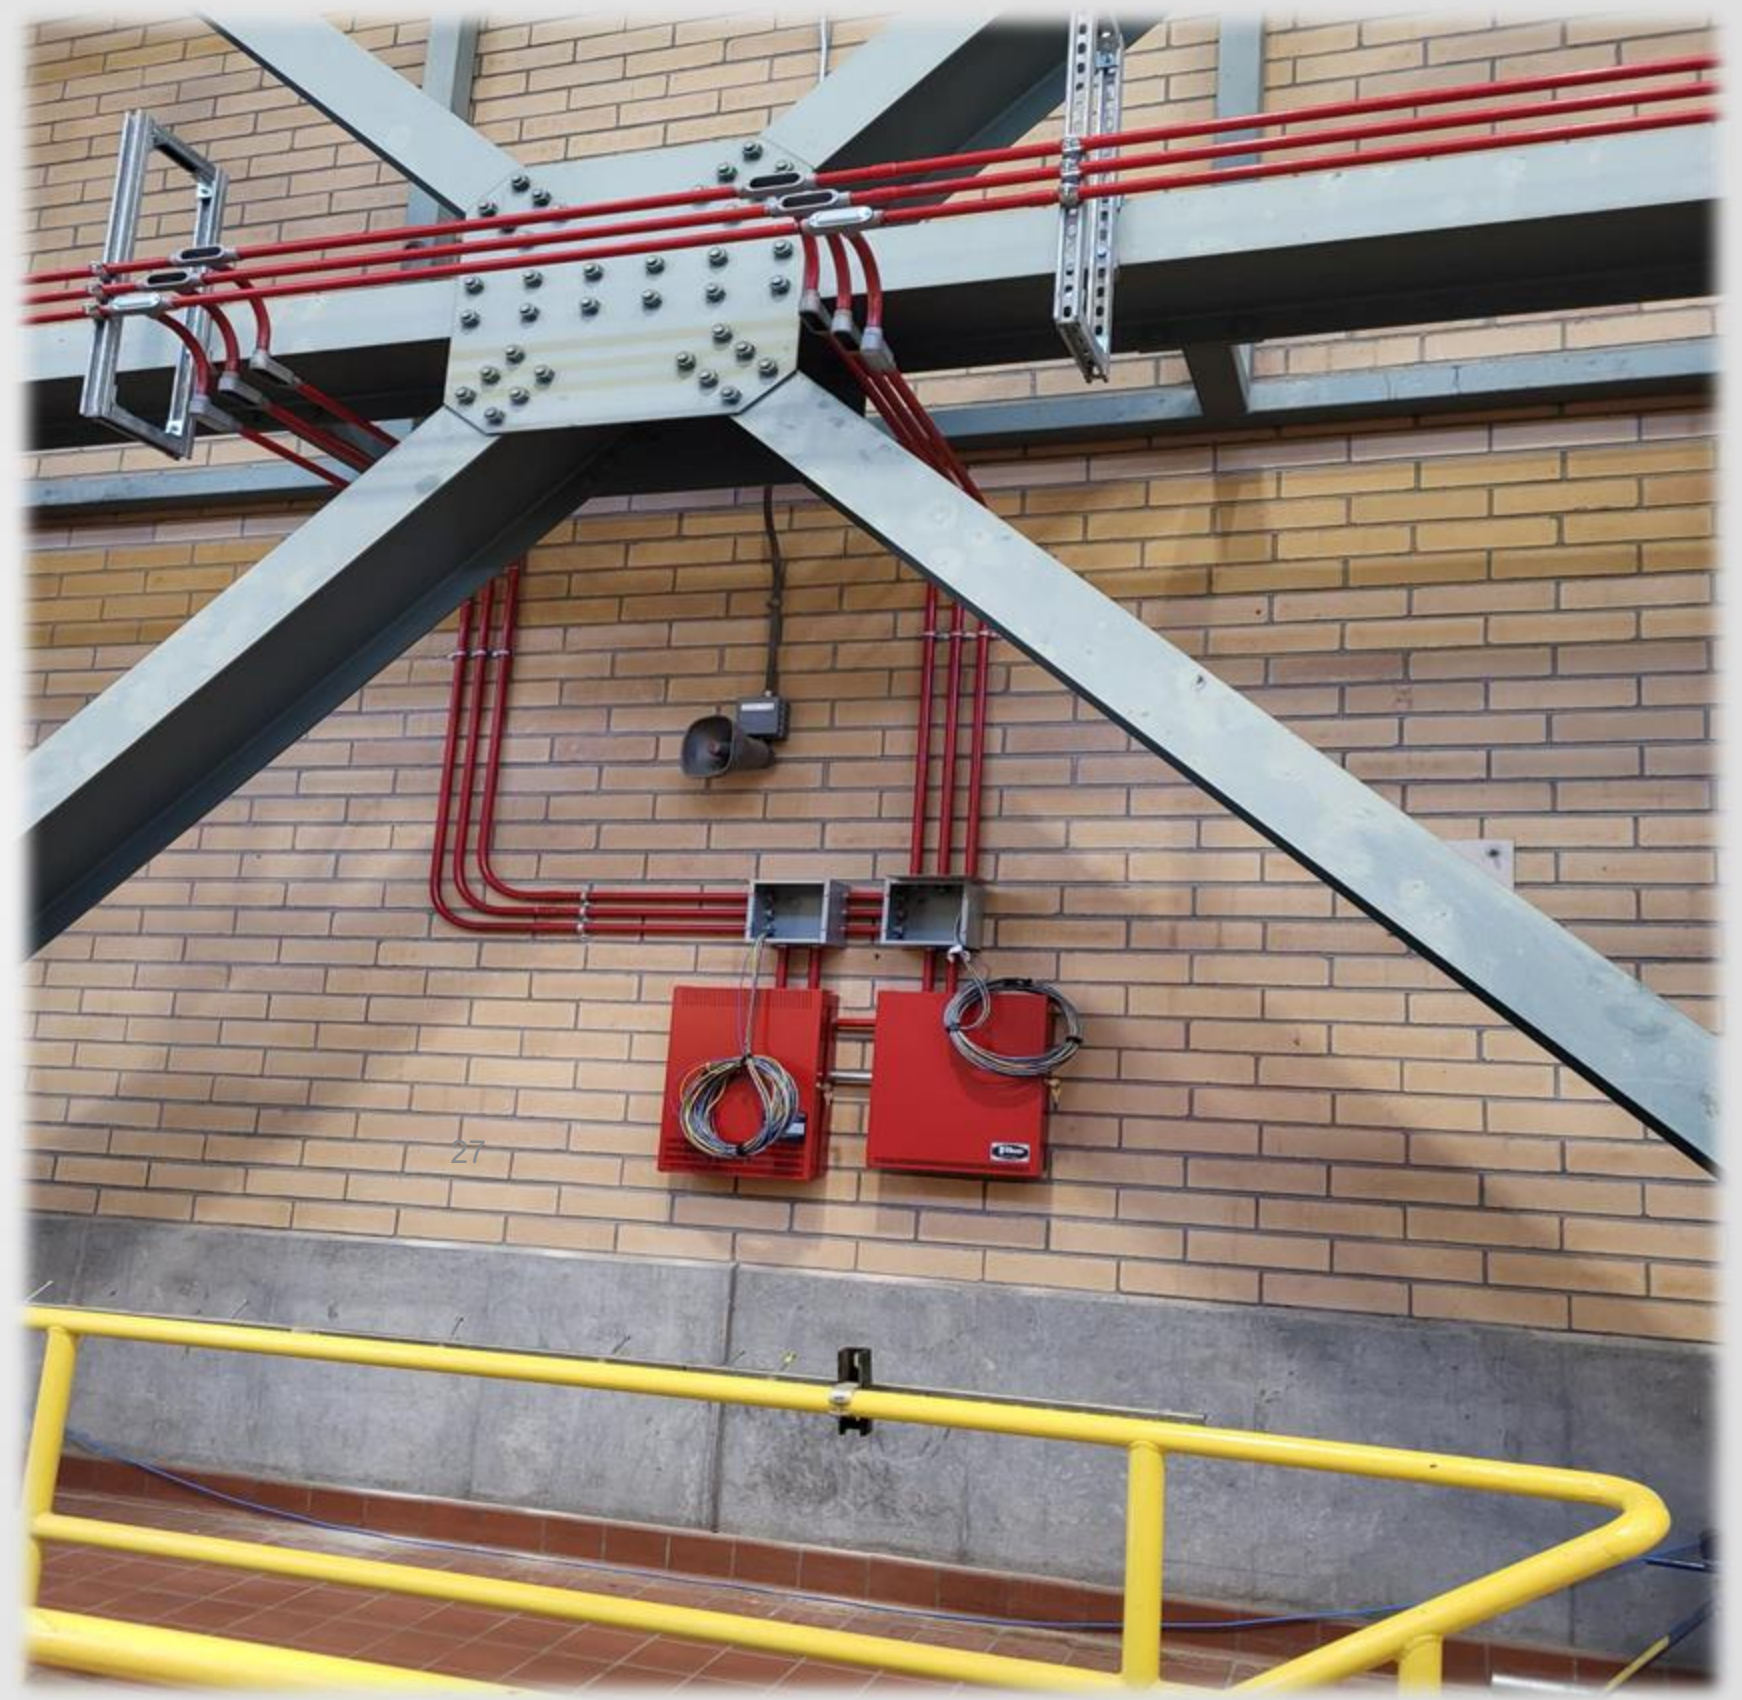

Fire Safety Modernization,
Gianelli P/G Plant, SLFD O&M Center, Dos Amigos PP, and Coalinga O&M Center

25-01 Temporary Rock Barriers



CALIFORNIA DEPARTMENT OF
WATER RESOURCES





25-01 Temporary Rock Barriers –
2025, 2026, 2027, Middle River, Old River and Grant Line Canal

Network: Jun 17, 2025 at 10:19:46 AM PDT
7793–7799 Undine Rd
Tracy CA 95206



25-01 Temporary Rock Barriers –
2025, 2026, 2027, Middle River, Old River and Grant Line Canal

Network: Jun 2, 2025 at 11:30:31 AM PDT
7793–7799 Undine Rd
Tracy CA 95206



25-01 Temporary Rock Barriers –
2025, 2026, 2027, Middle River, Old River and Grant Line Canal

Network: May 23, 2025 at 8:30:51 AM PDT
17001 Finck Rd
Tracy CA 95304



25-01 Temporary Rock Barriers –
2025, 2026, 2027, Middle River, Old River and Grant Line Canal

2025 State Water Project Construction Project Updates

Thank You!
